


John S. Meek Company Inc.
Kingsbridge Progress Schedule



John S. Meek Company Inc.
Kingsbridge Progress Schedule

ID	Task Name	Duration	Start	Finish	Predecessors	% Complete		September	October
45	DRILL AND INSTALL TIEBACKS	40 days	Thu 6/18/15	Wed 8/12/15	43,44	0%			
46	REMOVE MATERIAL DISPOSAL, CONCRETE, SOIL, ETC.	20 days	Thu 6/18/15	Wed 7/15/15	43,44	0%			
47	TEST TIEBACKS	20 days	Thu 7/16/15	Wed 8/12/15	45FS-20 days	0%			
48	INSTALL CONCRETE WALE FALSEWORK	3 days	Thu 8/13/15	Mon 8/17/15	47,46,23,25	0%			
49	SAWCUT/CHIP TOP & BOTTOM KEY FOR CONCRETE WALE	5 days	Tue 8/18/15	Mon 8/24/15	48	0%			
50	DRILL/EPOXY DOWELS INTO EXISTING CONCRETE WALE	5 days	Tue 8/18/15	Mon 8/24/15	48	0%			
51	INSTALL REINFORCEMENT STEEL FOR CONCRETE WALE	2 days	Tue 8/25/15	Wed 8/26/15	50,49	0%			
52	FORM CONCRETE WALE	3 days	Thu 8/27/15	Mon 8/31/15	51	0%			
53	POUR CONCRETE WALE	1 day	Tue 9/1/15	Tue 9/1/15	52	0%			
54	CURE CONCRETE WALE	7 days	Wed 9/2/15	Fri 9/11/15	53	0%			
55	STRIP FORMS/FALSEWORK CONCRETE WALE	5 days	Mon 9/14/15	Fri 9/18/15	54,17	0%			
56	REPLACE REMOVED INTERFERING PORTIONS OF EXISTING DECKS	3 days	Mon 9/21/15	Wed 9/23/15	55	0%			
57	INSTALL REMOVED PILING/GANGWAYS	1 day	Thu 9/24/15	Thu 9/24/15	56,11,13	0%			
58	DEMOBILIZE/CLEANUP	3 days	Fri 9/25/15	Tue 9/29/15	57	0%			

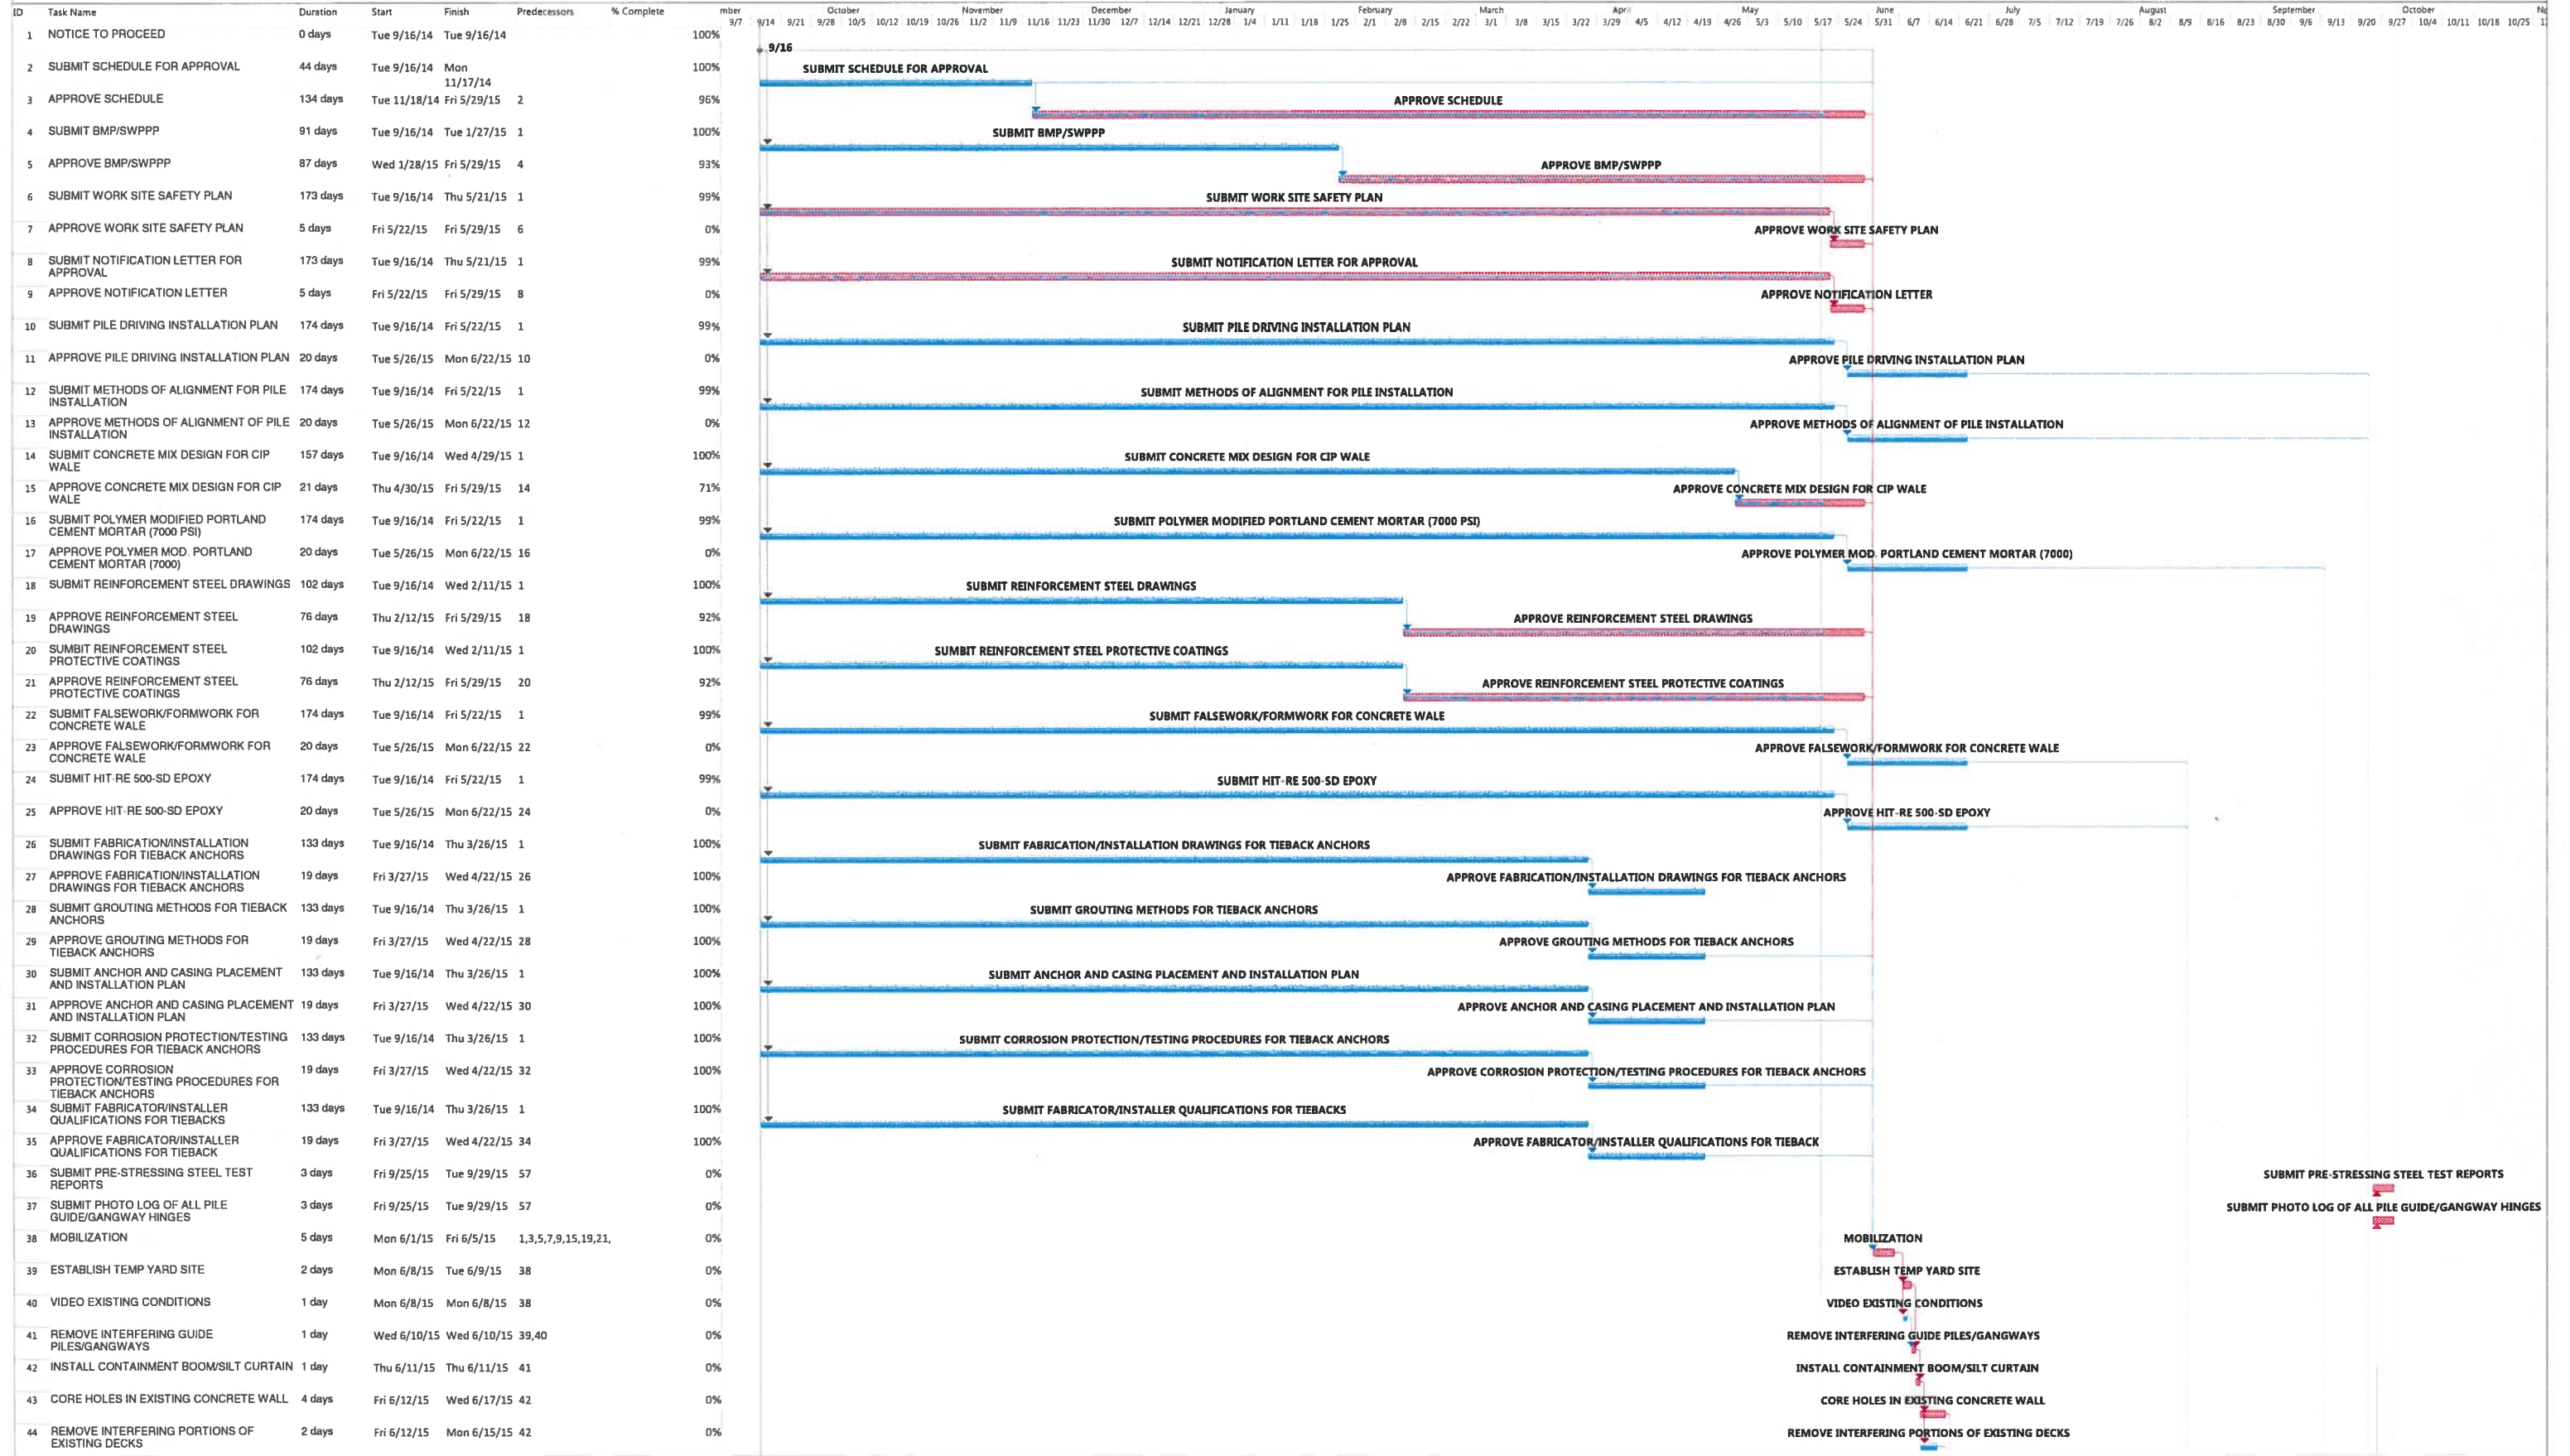
